


A. Site Energy Production Summary*

Energy Production (kWh)					
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	WTG 1	WTG 2	WTG 3
Apr-24	1,335,000	696,296	320,266	107,262	268,768
May-24	1,106,000	725,087	270,871	206,159	248,057
Jun-24	836,000	766,124	281,287	214,562	270,275
Jul-24	694,000	444,201	169,239	124,259	150,703
Aug-24	619,000	509,797	191,511	135,123	183,163
Sep-24	839,000	652,549	236,771	178,198	237,580
Oct-24	1,294,000	965,209	362,265	268,971	333,973
Nov-24	1,428,000	1,146,109	404,011	340,300	401,798
Dec-24	1,459,000	1,275,535	426,875	420,969	427,691
Jan-25	1,589,000	1,633,392	585,943	490,527	556,922
Feb-25	1,306,000	790,457	278,380	244,880	267,197
Mar-25	1,331,000	1,736,848	617,707	532,296	586,845
Apr-25	1,335,000	0			
Production 2025 (ytd) (kWh)	4,226,000	4,160,697	1,482,030	1,267,703	1,410,964
Total Production (LTM) (kWh)	13,836,000	11,341,604	4,145,126	3,263,506	3,932,972
Capacity Factor (LTM)	28.77%				

B. Site Energy Production Graph

March-2025

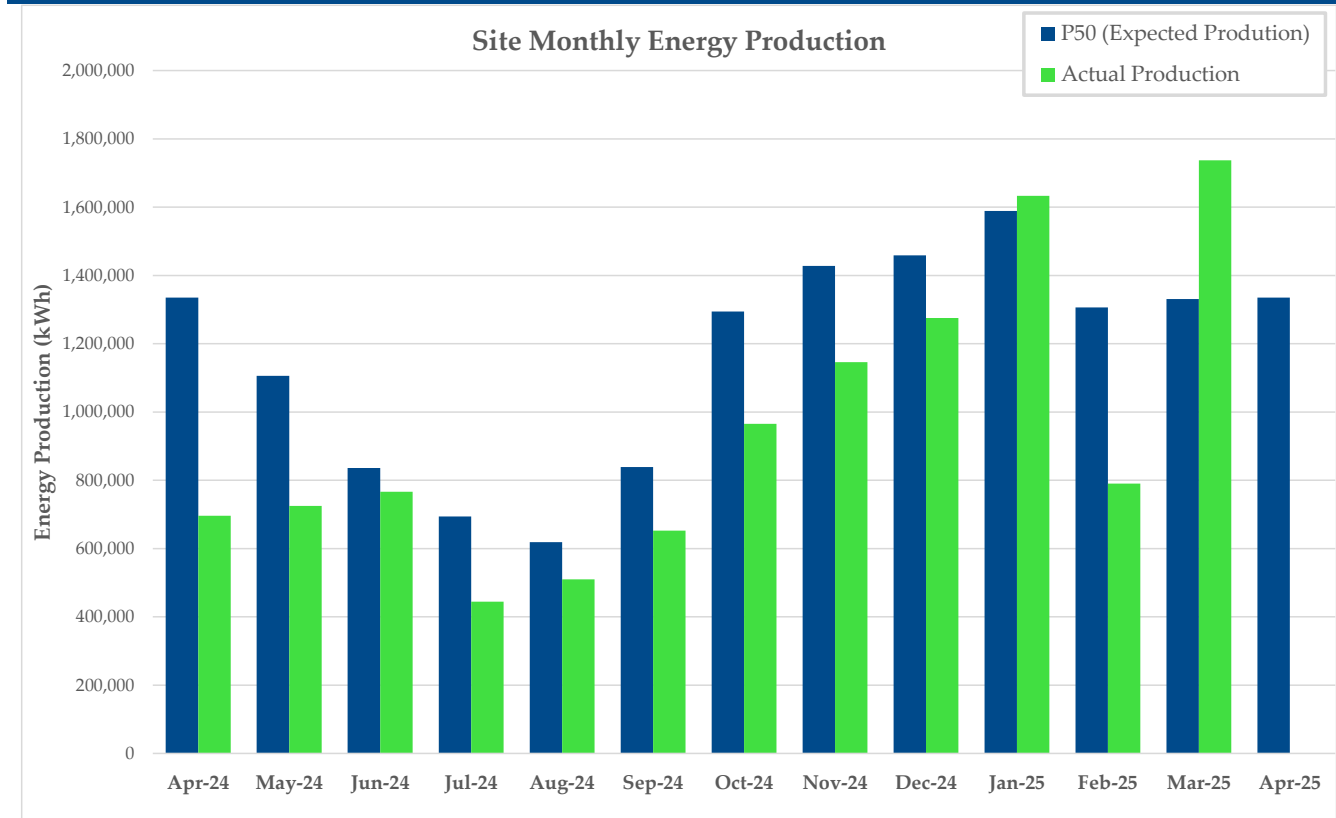

Monthly Report
March-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2025	1 Year Preventive Maintenance	~15	WTG 1
September-2025	1 Year Preventive Maintenance	~15	WTG 2
September-2025	1 Year Preventive Maintenance	~15	WTG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/8/2025	Weather Shutdown	Unplanned	12.14	WTG 1
3/8/2025	Weather Shutdown	Unplanned	11.68	WTG 2
3/8/2025	Weather Shutdown	Unplanned	15.86	WTG 3
3/10/2025	.5 Year Semi-Annual Maintenance	Planned	3.44	WTG 1
3/10/2025	.5 Year Semi-Annual Maintenance	Planned	4.95	WTG 2
3/10/2025	.5 Year Semi-Annual Maintenance	Planned	1.07	WTG 3
3/19/2025	Turbine Fault	Unplanned	14.07	WTG 3
3/19/2025-3/20/2025	Weather Shutdown	Unplanned	4.61	WTG1,WTG2, WTG3
3/26/2025	.5 Year Semi-Annual Maintenance	Planned	2.75	WTG 1
3/26/2025	.5 Year Semi-Annual Maintenance	Planned	5.41	WTG 3
3/27/2025	.5 Year Semi-Annual Maintenance	Planned	5.74	WTG 1
3/27/2025	.5 Year Semi-Annual Maintenance	Planned	3.96	WTG 2

F. Turbine Downtime ¹

Downtime (hr)	This Month	Year To Date
WTG 1	31.29	187.25
WTG 2	26.34	168.98
WTG 3	45.22	204.66
Total	102.85	560.89

G. Billed Data

Meter Reading (Date/Time)	4/1/2025 12:00 AM
Meter To Date Produced	11,196,362
Meter To Date Consumed	37,612
Last Reading Produced	9,474,686
Last Reading Consumed	36,538
Billed kWh	1,720,602 kWh
Next Meter Reading	5/1/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² Turbines were actively generating starting these days:
WTG 1 - April 10
WTG 2 - April 18
WTG 3 - April 9
Energy generation was billed to the customer starting April 18, 2024

³ WTG 3 was derated to 1000 kW for 22.28 hrs March 28-March 29.
