



HARPSTER WIND PROJECT


Harpster, OH

A. Site Energy Production Summary

	Energy Production (kWh)	
	Site	
	P50 (Expected Production)	Actual Production
Mar-24	417,000	0 ²
Apr-24	399,000	71,938
May-24	311,000	176,362
Jun-24	228,000	182,891
Jul-24	179,000	130,160
Aug-24	157,000	115,765
Sep-24	224,000	147,046
Oct-24	338,000	226,873
Nov-24	402,000	312,105
Dec-24	403,000	344,484
Jan-25	460,000	442,965
Feb-25	372,000	254,448
Mar-25	417,000	437,434
Production 2025 (ytd) (kWh)	1,249,000	1,134,847
Total Production (LTM) (kWh)	3,890,000	2,842,471
Capacity Factor (LTM)	21.63%	

B. Site Energy Production Graph

March-2025

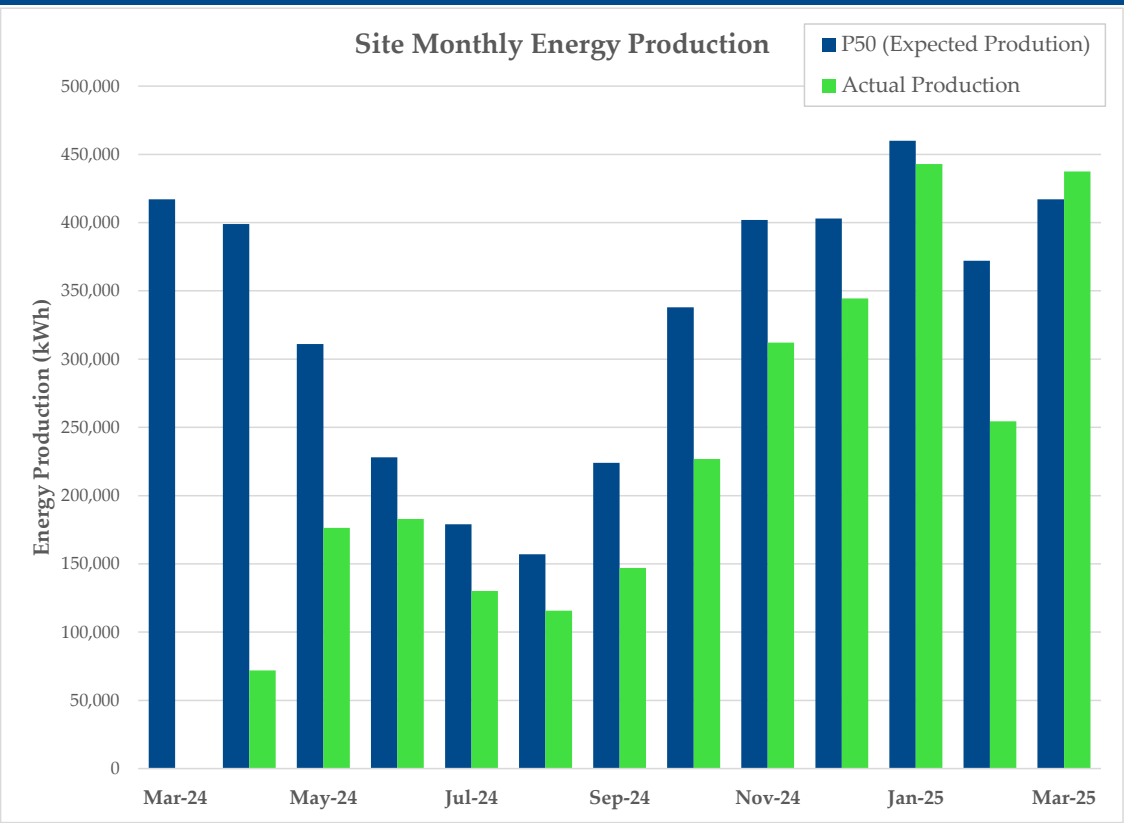

Monthly Report

March-2025



C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2025	9 Year Preventive Maintenance	~15	H1

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/1/2025-3/3/2025	Turbine Fault	Unplanned	58.17	H1
3/16/2025-3/18/2025	Turbine Fault	Unplanned	48.71	H1
3/18/2025	8.5 Year Preventive Maintenance	Planned	6.00	H1
3/31/2025	Turbine Fault	Unplanned	8.47	H1

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
H1	126.61	223.75

G. Billed Data

Meter Reading (Date/Time)	3/27/2025 12:00 AM
Meter To Date Produced	28,693,174 kWh
Meter To Date Consumed	109,977 kWh
Last Reading Produced	28,288,566 kWh
Last Reading Consumed	108,937 kWh
Billed kWh	403,568 kWh
Next Meter Reading	4/26/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, the project had no energy production in March 2024.
