


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
Mar-24	802,000	0	0	0
Apr-24	951,000	231,529	116,676	114,853
May-24	601,000	464,507	229,425	235,082
Jun-24	425,000	469,571	236,472	233,099
Jul-24	390,000	301,440	152,091	149,349
Aug-24	399,000	280,180	140,866	139,314
Sep-24	337,000	370,064	187,230	182,834
Oct-24	637,000	572,084	289,438	282,646
Nov-24	834,000	785,699	390,357	395,342
Dec-24	1,015,000	893,806	444,191	449,615
Jan-25	875,000	1,030,662	504,989	525,673
Feb-25	917,000	541,951	268,768	273,183
Mar-25	802,000	1,129,812	567,643	562,169
Production 2025 (ytd) (kWh)	2,594,000	2,702,425	1,341,400	1,361,025
Total Production (LTM) (kWh)	8,183,000	7,071,305	3,528,146	3,543,159
Capacity Factor (LTM)	26.91%			

B. Site Energy Production Graph

March-2025

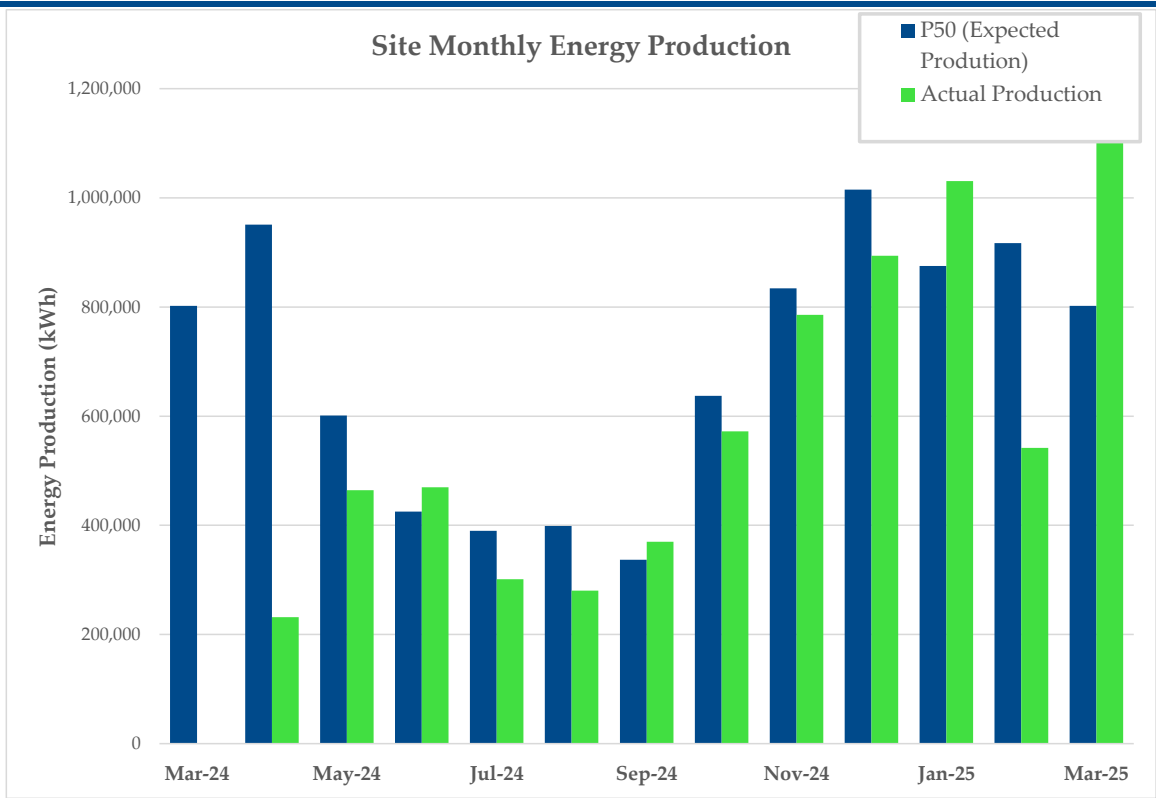

Monthly Report
March-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
April-2025	9 Year Preventive Maintenance	~15	W1
April-2025	9 Year Preventive Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/8/2025	Weather shutdown	Unplanned	4.10	W1, W2

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
W1	8.72	208.20
W2	7.46	136.62
Total	16.18	344.82

G. Billed Data

Meter Reading (Date/Time)	3/29/2025 12:00 AM
Meter To Date Produced	68,340,497 kWh
Meter To Date Consumed	158,870 kWh
Last Reading Produced	67,349,141 kWh
Last Reading Consumed	158,462 kWh
Billed kWh	990,948 kWh
Next Meter Reading	4/29/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending

² As a result of previously disclosed circumstances, the project had no energy production February 2024 - March 2024.
