


A. Site Energy Production Summary

		Energy Production (kWh)				
		Site		By Turbine		
		P50 (Expected Production)	Actual Production	V1	V2	
	Mar-24	777,000	0	0	0	2
	Apr-24	722,000	0	0	0	2
	May-24	564,000	0	0	0	2
	Jun-24	422,000	26,106	0	26,106	3
	Jul-24	351,000	270,166	124,029	146,137	
	Aug-24	303,000	261,120	136,201	124,919	
	Sep-24	431,000	390,486	185,589	204,897	
	Oct-24	674,000	522,777	233,362	289,415	
	Nov-24	796,000	678,634	359,728	318,906	
	Dec-24	820,000	821,736	388,737	432,999	
	Jan-25	931,000	988,728	488,844	499,884	
	Feb-25	737,000	528,117	268,790	259,327	
	Mar-25	777,000	1,057,937	508,748	549,189	
Production 2025 (ytd) (kWh)		2,445,000	2,574,782	1,266,382	1,308,400	
Total Production (LTM) (kWh)		7,528,000	5,545,807	2,694,028	2,851,779	
Capacity Factor (LTM)		21.10%				

B. Site Energy Production Graph

March-2025

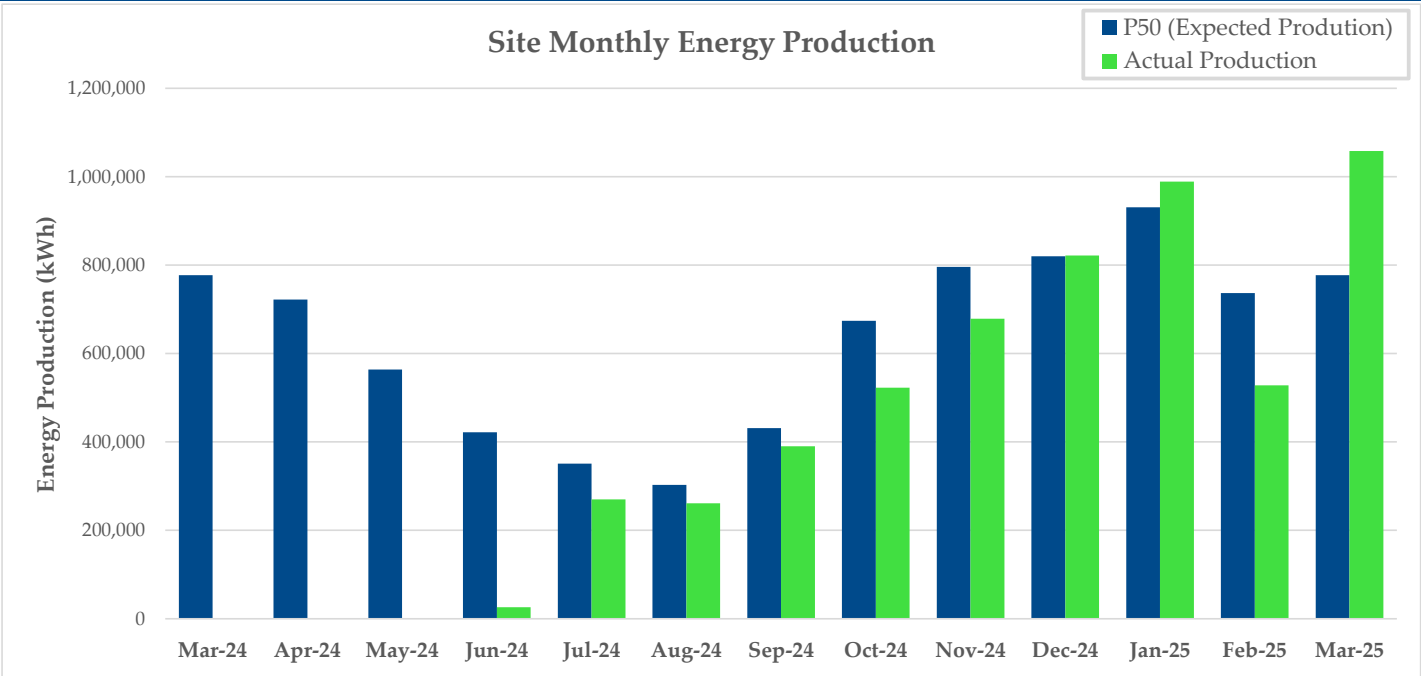

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2025	6.5 Year Maintenance	~8	V1
September-2025	6.5 Year Maintenance	~8	V2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
3/5/2025-3/7/2025	Turbine Fault	Unplanned	45.22	V1
3/12/2025	6 Year Maintenance	Planned	7.75	V1
3/13/2025	6 Year Maintenance	Planned	5.66	V2

F. Downtime¹

Downtime (hr)	This Month	Year To Date
V1	59.64	191.46
V2	7.02	158.77
Total	66.66	350.23

G. Billed Data

Meter Reading (Date/Time)	4/1/2025 12:00 AM
Meter To Date Produced	44,038,038 kWh
Meter To Date Consumed	124,539 kWh
Last Reading Produced	43,008,916 kWh
Last Reading Consumed	124,017 kWh
Billed kWh	1,028,600 kWh
Next Meter Reading	5/1/2025 12:00 AM

H. Report Notes and Comments

¹Turbine Availability/Downtime Pending.

²As a result of previously disclosed circumstances, the project had no energy production February 2024 - May 2024.

³As a result of previously disclosed circumstances, V1 had no energy production February 2024 - June 2024.
