


A. Site Energy Production Summary*

	Energy Production (kWh)					
	Site		By Turbine			
	P50 (Expected Production)	Actual Production	WTG 1	WTG 2	WTG 3	
Apr-24	1,335,000	696,296	320,266	107,262	268,768	2
May-24	1,106,000	725,087	270,871	206,159	248,057	
Jun-24	836,000	766,124	281,287	214,562	270,275	
Jul-24	694,000	444,201	169,239	124,259	150,703	
Aug-24	619,000	509,797	191,511	135,123	183,163	
Sep-24	839,000	652,549	236,771	178,198	237,580	
Oct-24	1,294,000	965,209	362,265	268,971	333,973	
Nov-24	1,428,000	1,146,109	404,011	340,300	401,798	
Dec-24	1,459,000	1,275,535	426,875	420,969	427,691	
Jan-25	1,589,000	1,633,392	585,943	490,527	556,922	
Feb-25	1,306,000	790,457	278,380	244,880	267,197	3
Mar-25	1,331,000	1,736,848	617,707	532,296	586,845	
Apr-25	1,335,000	1,077,275	388,957	321,953	366,365	3
Production 2025 (ytd) (kWh)	5,561,000	5,237,972	1,870,987	1,589,656	1,777,329	
Total Production (LTM) (kWh)	13,836,000	11,722,583	4,213,817	3,478,197	4,030,569	
Capacity Factor (LTM)	29.74%					

B. Site Energy Production Graph

April-2025

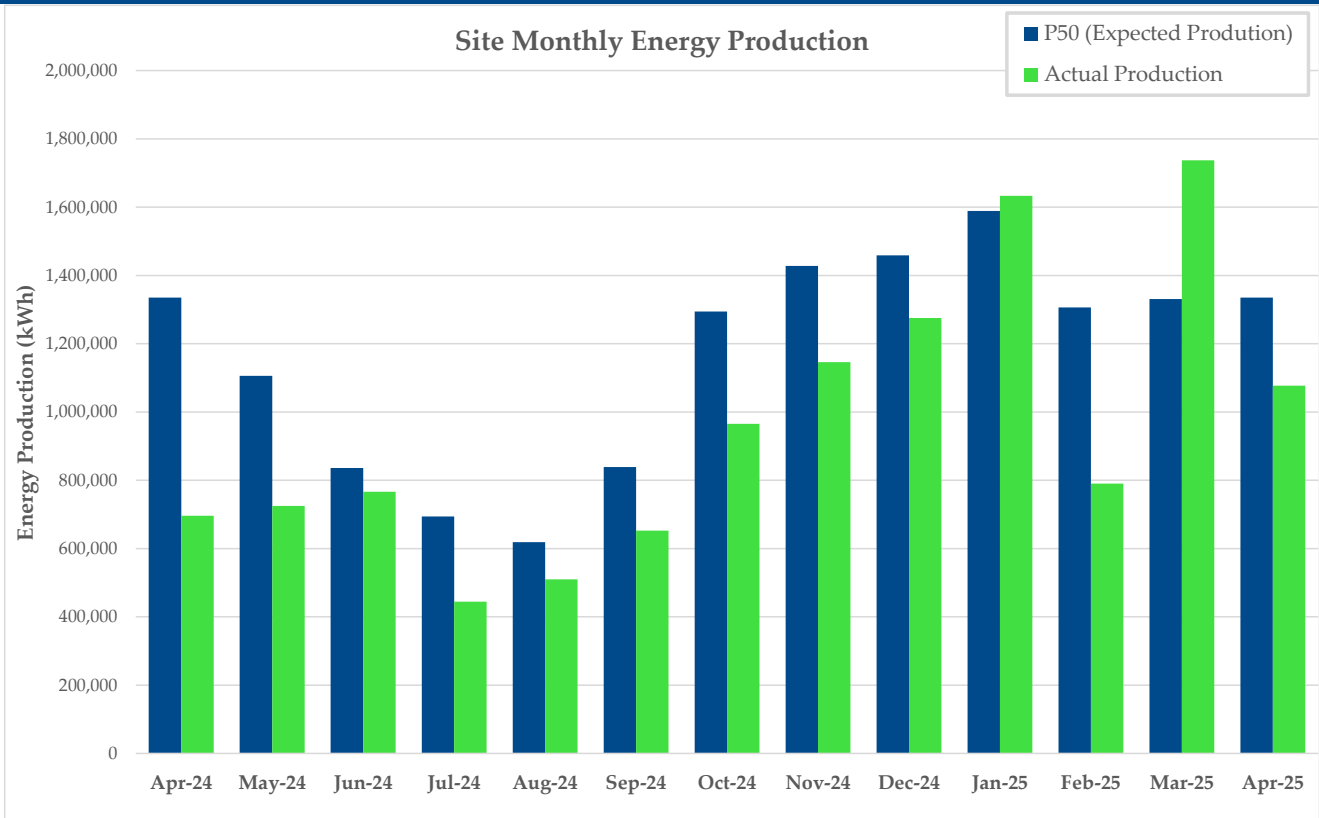

Monthly Report
April-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2025	1 Year Preventive Maintenance	~15	WTG 1
September-2025	1 Year Preventive Maintenance	~15	WTG 2
September-2025	1 Year Preventive Maintenance	~15	WTG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
4/2/2025-4/3/2025	Weather Shutdown	Unplanned	15.36	WTG 1, WTG 2
4/2/2025-4/3/2025	Turbine Fault	Unplanned	25.63	WTG 3
4/5/2025-4/7/2025	Turbine Fault	Unplanned	48.68	WTG 3

F. Turbine Downtime ¹

Downtime (hr)	This Month	Year To Date
WTG 1	20.10	207.35
WTG 2	18.20	187.18
WTG 3	75.58	280.24
Total	113.88	674.77

G. Billed Data

Meter Reading (Date/Time)	5/1/2025 12:00 AM
Meter To Date Produced	12,260,310
Meter To Date Consumed	39,399
Last Reading Produced	11,196,362
Last Reading Consumed	37,612
Billed kWh	1,062,161 kWh
Next Meter Reading	6/1/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² Turbines were actively generating starting these days:

WTG 1 - April 10

WTG 2 - April 18

WTG 3 - April 9

Energy generation was billed to the customer starting April 18, 2024

³ WTG 3 was derated to 1000 kW for 22.28 hrs March 28-March 29

³WTG 3 was derated to 1000 kW for 27.98 hrs April 2-April 3

³WTG 3 was derated to 1000 kW for 43.58hrs April5-April 7
