


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	Expected Production	Actual Production	WTG 1	WTG 2	WTG 3
May-24	980,450	836,173	284,799	275,439	275,935
Jun-24	649,158	897,472	318,609	299,454	279,409
Jul-24	618,687	494,646	168,488	159,103	167,055
Aug-24	559,508	495,719	172,033	156,575	167,111
Sep-24	603,085	666,318	219,662	225,740	220,916
Oct-24	967,926	968,509	327,746	315,257	325,506
Nov-24	1,362,692	1,392,792	449,512	465,936	477,344
Dec-24	1,254,397	1,505,421	506,487	488,779	510,155
Jan-25	1,290,968	1,781,496	600,395	573,604	607,497
Feb-25	1,170,349	1,122,014	379,422	360,728	381,864
Mar-25	1,227,217	1,980,804	656,419	657,823	666,562
Apr-25	1,438,497	1,381,940	460,087	466,384	455,469
May-25	980,450	976,885	328,058	325,817	323,010
Production 2025 (ytd) (kWh)	6,107,482	7,243,139	2,424,381	2,384,356	2,434,402
Total Production (LTM) (kWh)	12,122,935	13,664,016	4,586,918	4,495,200	4,581,898
Capacity Factor (LTM)	34.66%				

B. Site Energy Production Graph

May-2025

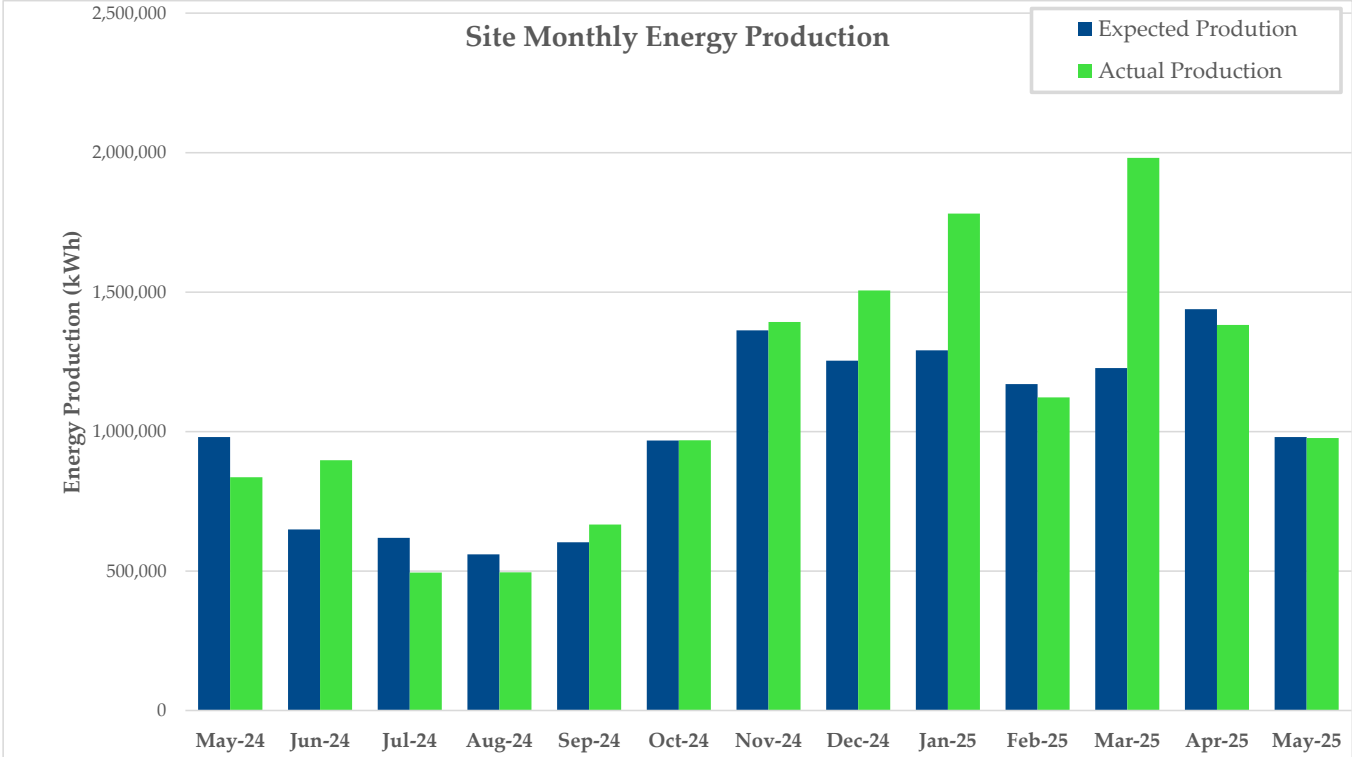

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
October-2025	13 Year Maintenance	~15	WTG 1
October-2025	13 Year Maintenance	~15	WTG 2
October-2025	13 Year Maintenance	~15	WTG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/21/2025-5/22/2025	Grid Fault	Unplanned	18.20	WTG 1, WTG 2, WTG 3

F. Turbine Downtime ¹

Downtime (hr)	This Month	Year To Date
WTG 1	18.20	60.46
WTG 2	18.20	40.50
WTG 3	20.59	100.18
Total	56.99	201.14

G. Wind Speed & Capacity Factor ²

Wind Speed (mph)	This Month	2024 Annual
WTG 1	4.94	4.94
WTG 2	4.90	4.90
WTG 3	4.97	4.97
Estimated	13.57	13.39

Capacity Factor (%)	This Month	2024 Annual
WTG 1	29.40%	42.25%
WTG 2	29.20%	41.45%
WTG 3	28.94%	40.09%
Low Estimate	28.39%	28.72%

H. Report Notes and Comments

¹ Turbine Downtime/Availability Pending

²Wind Speed Pending
