


A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z4	Z5	Z6
May-24	876,000	0	0	0	0
Jun-24	637,000	26,101	26,101	0	0
Jul-24	518,000	179,993	142,016	37,977	0
Aug-24	448,000	292,342	145,491	146,851	0
Sep-24	617,000	353,095	175,829	177,266	0
Oct-24	956,000	541,507	275,869	265,638	0
Nov-24	1,107,000	688,676	335,398	353,278	0
Dec-24	1,098,000	881,937	435,966	445,971	0
Jan-25	1,251,000	1,333,065	491,894	490,120	351,051
Feb-25	1,044,000	803,342	281,085	283,032	239,225
Mar-25	1,119,000	1,598,073	514,848	529,665	553,560
Apr-25	1,116,000	1,020,164	348,368	350,865	320,931
May-25	876,000	877,306	288,333	284,509	304,464
Production 2025 (ytd) (kWh)	5,406,000	5,631,950	1,924,528	1,938,191	1,769,231
Total Production (LTM) (kWh)	10,787,000	8,595,601	3,461,198	3,365,172	1,769,231
Capacity Factor (LTM)	21.81%				

B. Site Energy Production Graph

May-2025

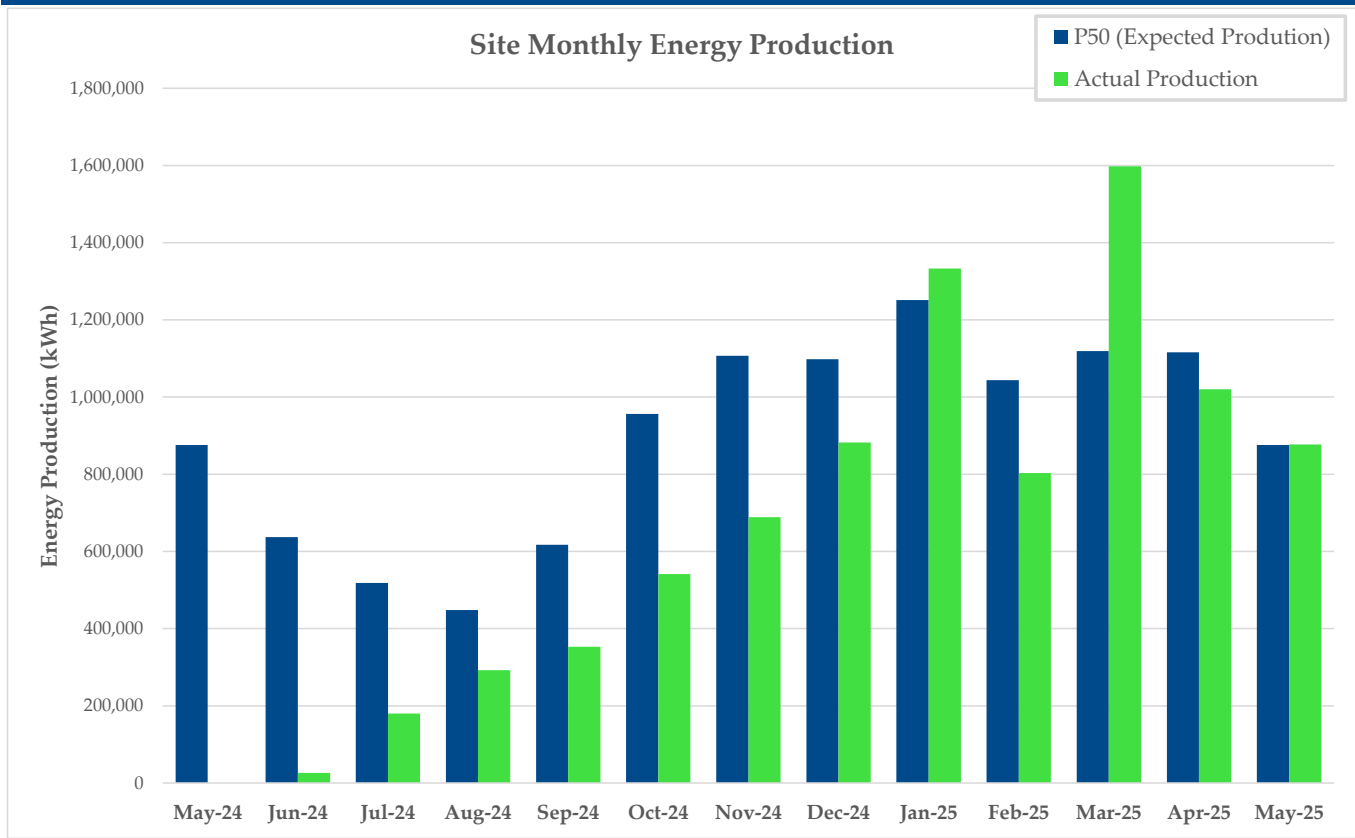

Monthly Report
May-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	1

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
July-2025	4.5 Year Preventive Maintenance	~15	Z4
July-2025	4.5 Year Preventive Maintenance	~15	Z5
July-2025	4.5 Year Preventive Maintenance	~15	Z6

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
------	-------	-------------------	----------------	---------

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
Z4	4.21	162.13
Z5	4.25	99.08
Z6	4.28	424.54
Total	12.74	685.75

G. Billed Data

Meter Reading (Date/Time)	5/20/2025 12:00 AM
Ball 2.0 Production (This Period)	994,527 kWh
Ball 2.0 Consumption (This Period)	1,930 kWh
Billed kWh	992,597 kWh
Next Meter Reading	6/19/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, the project's energy production was limited beginning 01/22/2024. Z4 resumed operation on 6/28/2024 and Z5 resumed operation on 7/23//2024.

³ Z6 Repair Complete. Resumed operation on 1/6/2025. Monthly production total includes 189 kWh from testing on 1/3/2025.

⁴ Z6 was Derated to 1000 kW for 44.15 hours on March 14 - March 16.

⁵ Z6 was Derated to 1000 kW for 63.74 hours on April 21-April 24.
