


A. Site Energy Production Summary

	Energy Production (kWh)			
	Site		By Turbine	
	P50 (Expected Production)	Actual Production	W1	W2
May-24	601,000	464,507	229,425	235,082
Jun-24	425,000	469,571	236,472	233,099
Jul-24	390,000	301,440	152,091	149,349
Aug-24	399,000	280,180	140,866	139,314
Sep-24	337,000	370,064	187,230	182,834
Oct-24	637,000	572,084	289,438	282,646
Nov-24	834,000	785,699	390,357	395,342
Dec-24	1,015,000	893,806	444,191	449,615
Jan-25	875,000	1,030,662	504,989	525,673
Feb-25	917,000	541,951	268,768	273,183
Mar-25	802,000	1,129,812	567,643	562,169
Apr-25	951,000	699,169	361,078	338,091
May-25	601,000	577,922	289,767	288,155
Production 2025 (ytd) (kWh)	4,146,000	3,979,516	1,992,245	1,987,271
Total Production (LTM) (kWh)	8,183,000	7,652,360	3,832,890	3,819,470
Capacity Factor (LTM)	29.12%			

B. Site Energy Production Graph

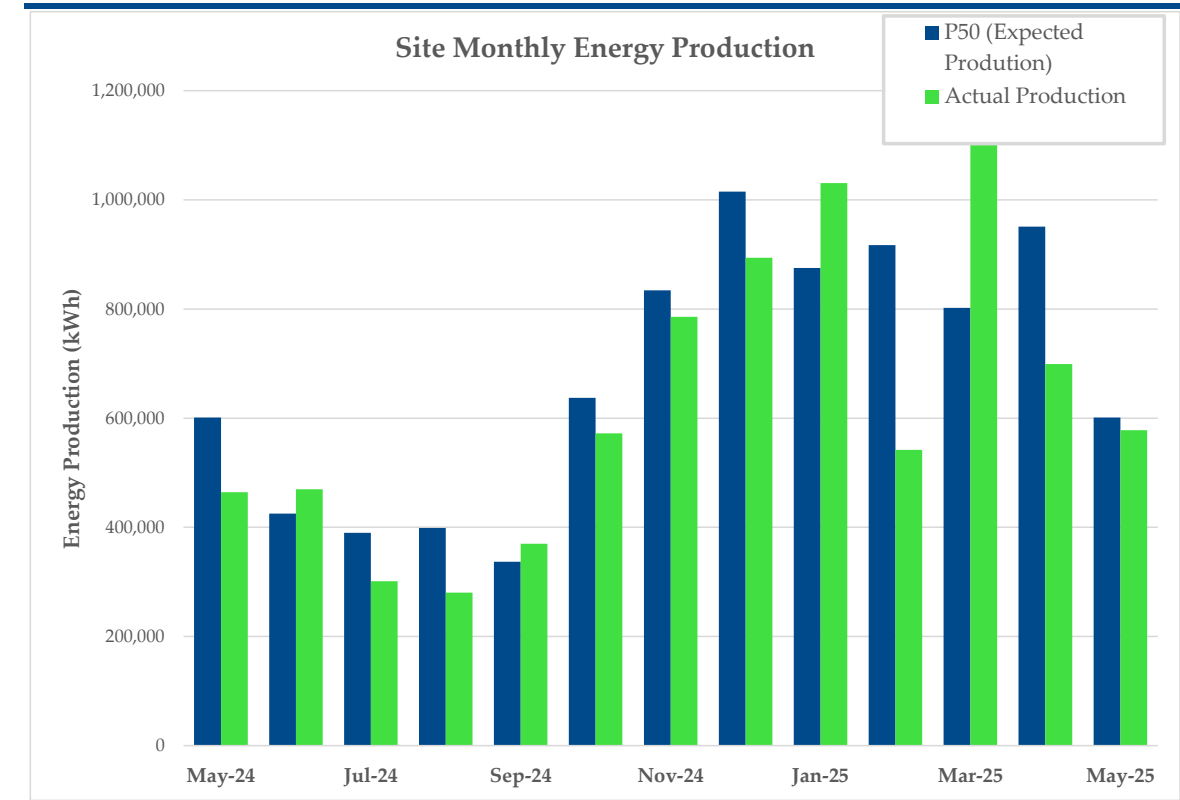

Monthly Report

May-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2025	9.5 Year Preventive Maintenance	~15	W1
September-2025	9.5 Year Preventive Maintenance	~15	W2

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/12/2025-5/13/2025	Turbine Fault	Unplanned	13.85	W2

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
W1	5.18	224.89
W2	17.80	228.02
Total	22.98	452.91

G. Billed Data

Meter Reading (Date/Time)	5/29/2025 12:00 AM
Meter To Date Produced	69,681,465 kWh
Meter To Date Consumed	160,802 kWh
Last Reading Produced	69,087,431 kWh
Last Reading Consumed	159,912 kWh
Billed kWh	593,144 kWh
Next Meter Reading	6/29/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending
