


A. Site Energy Production Summary

	Energy Production (kWh)					
	Site		By Turbine			
	P50 (Expected Production)	Actual Production	WG1	WG2	WG3	
May-24	974,000	443,966	224,384	0	219,582	2
Jun-24	714,000	457,519	234,750	0	222,769	2
Jul-24	566,000	306,010	138,508	26,329	141,173	
Aug-24	514,000	412,680	141,710	134,341	136,629	
Sep-24	716,000	531,587	183,534	168,417	179,636	
Oct-24	1,051,000	881,013	307,605	290,645	282,763	
Nov-24	1,224,000	1,122,327	391,525	369,519	361,283	
Dec-24	1,217,000	1,260,023	446,812	416,052	397,159	
Jan-25	1,343,000	1,398,943	512,624	450,432	435,887	
Feb-25	1,133,000	710,891	253,926	229,140	227,825	3
Mar-25	1,312,000	1,642,126	558,314	545,778	538,034	
Apr-25	1,272,000	1,161,033	398,359	383,282	379,392	
May-25	974,000	820,580	290,223	244,974	285,383	
Production 2025 (ytd) (kWh)	6,034,000	5,733,573	2,013,446	1,853,606	1,866,521	
Total Production (LTM) (kWh)	12,036,000	10,704,732	3,857,890	3,258,909	3,587,933	
Capacity Factor (LTM)	27.16%					

B. Site Energy Production Graph

May-2025

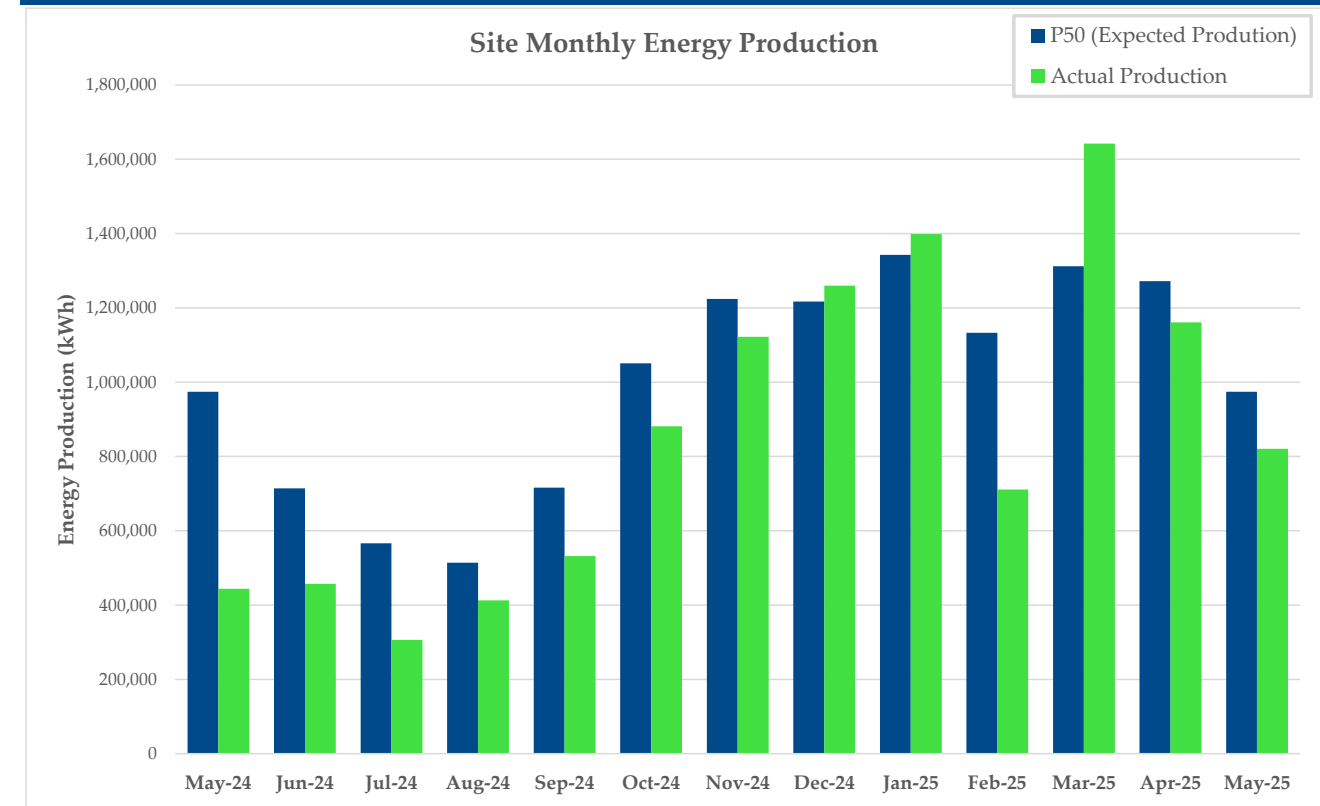

Monthly Report May-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
July-2025	6.5 Year Preventive Maintenance	~15	WG 1
July-2025	6.5 Year Preventive Maintenance	~15	WG 2
July-2025	6.5 Year Preventive Maintenance	~15	WG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
5/16/2025	Weather Shutdown	Unplanned	5.56	WG 1, WG 3
5/16/2025-5/19/2025	Turbine Fault	Unplanned	64.09	WG 2
5/21/2025	Turbine Fault	Unplanned	6.83	WG 2

F. Turbine Downtime¹

Downtime (hr)	This Month	Year To Date
WG1	8.63	214.86
WG2	72.67	250.21
WG3	8.38	200.52
`	89.68	665.59

G. Billed Data

Meter Reading (Date/Time)	5/29/2025 12:00 AM
Meter To Date Produced	67,753,140 kWh
Meter To Date Consumed	280,070 kWh
Last Reading Produced	66,943,253 kWh
Last Reading Consumed	277,285 kWh
Billed kWh	807,102 kWh
Next Meter Reading	6/29/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Availability/Downtime Pending.

² As a result of previously disclosed circumstances, WG 2 had no energy production February 2024 - June 2024.

³ WG2 was derated to 250 KW for .62hrs on Feb 13 for testing
