


A. Site Energy Production Summary*

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	WTG 1	WTG 2	WTG 3
Jun-24	836,000	766,124	281,287	214,562	270,275
Jul-24	694,000	444,201	169,239	124,259	150,703
Aug-24	619,000	509,797	191,511	135,123	183,163
Sep-24	839,000	652,549	236,771	178,198	237,580
Oct-24	1,294,000	965,209	362,265	268,971	333,973
Nov-24	1,428,000	1,146,109	404,011	340,300	401,798
Dec-24	1,459,000	1,275,535	426,875	420,969	427,691
Jan-25	1,589,000	1,633,392	585,943	490,527	556,922
Feb-25	1,306,000	790,457	278,380	244,880	267,197
Mar-25	1,331,000	1,736,848	617,707	532,296	586,845
Apr-25	1,335,000	1,077,275	388,957	321,953	366,365
May-25	1,106,000	866,072	300,572	243,799	321,701
Jun-25	836,000	661,220	184,021	214,709	262,490
Production 2025 (ytd) (kWh)	7,503,000	6,765,264	2,355,580	2,048,164	2,361,520
Total Production (LTM) (kWh)	13,836,000	11,758,664	4,146,252	3,515,984	4,096,428
Capacity Factor (LTM)	29.83%				

B. Site Energy Production Graph

June-2025

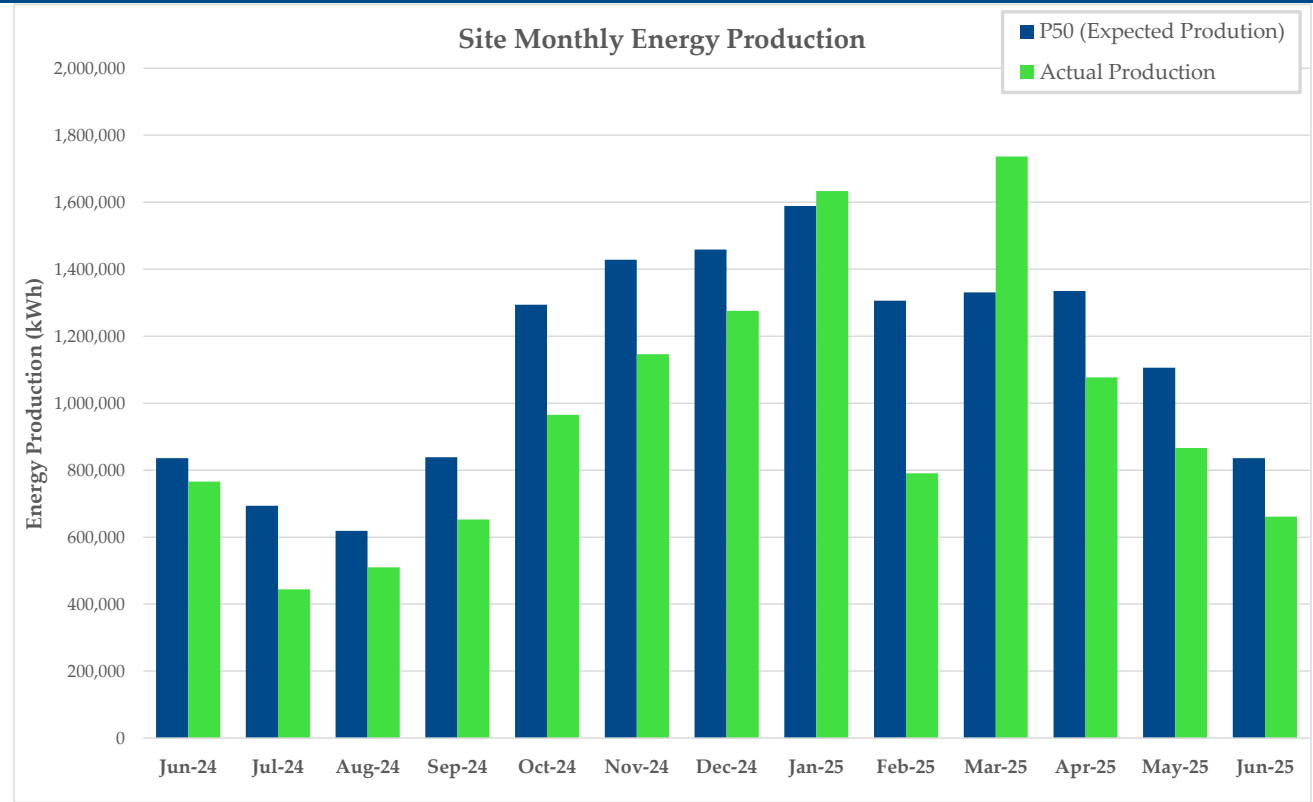

Monthly Report
June-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
September-2025	1 Year Preventive Maintenance	~15	WTG 1
September-2025	1 Year Preventive Maintenance	~15	WTG 2
September-2025	1 Year Preventive Maintenance	~15	WTG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
6/11/2025-6/13/2025	Turbine Fault	Unplanned	42.65	WTG 1
6/18/2025-6/20/2025	Turbine Fault	Unplanned	49.38	WTG 1
6/21/2025-6/22/2025	Turbine Fault	Unplanned	20.69	WTG 1
6/26/2025-6/27/2025	Turbine Fault	Unplanned	19.77	WTG 1
6/27/2025-6/30/2025	Turbine Fault	Unplanned	66.1	WTG 1
6/30/2025	Turbine Fault	Unplanned	9.25	WTG1

F. Turbine Downtime and Pending ¹

Downtime (hr)	This Month	Year To Date
WTG 1	210.94	470.76
WTG 2	8.92	204.49
WTG 3	5.96	289.77
Total	225.82	965.02

Uptime (hrs)	Life Time
WTG1, WTG2, WTG3	10224.00

G. Billed Data

Meter Reading (Date/Time)	7/1/2025 12:00 AM
Meter To Date Produced	13,762,700
Meter To Date Consumed	44,587
Last Reading Produced	13,113,274
Last Reading Consumed	41,848
Billed kWh	646,687 kWh
Next Meter Reading	8/1/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Downtime and Uptime Pending.

² WTG 3 was derated to 1000 kW for 22.28 hrs March 28-March 29

²WTG 3 was derated to 1000 kW for 27.98 hrs April 2-April 3

²WTG 3 was derated to 1000 kW for 43.58 hrs April5-April 7
