



BALL CORPORATION - ZEPHYR WIND PROJECT 1.0

North Findlay Wind Campus, Findlay, OH

Monthly Report
June-2025




A. Site Energy Production Summary

	Energy Production (kWh)				
	Site		By Turbine		
	P50 (Expected Production)	Actual Production	Z1	Z2	Z3
Jun-24	599,000	666,365	228,319	222,302	215,744
Jul-24	549,000	408,393	144,779	135,803	127,811
Aug-24	559,000	396,364	137,674	134,332	124,358
Sep-24	482,000	468,646	179,579	178,791	110,276
Oct-24	916,000	815,845	288,194	271,762	255,889
Nov-24	1,203,000	856,131	346,454	195,160	314,517
Dec-24	1,475,000	1,183,437	338,701	436,335	408,401 ²
Jan-25	1,260,000	1,498,704	519,090	499,488	480,126
Feb-25	1,310,000	777,633	278,062	278,866	220,705
Mar-25	1,140,000	1,627,608	577,430	552,966	497,212
Apr-25	1,359,000	1,017,888	335,455	344,738	337,695
May-25	856,000	836,841	290,425	275,972	270,444
Jun-25	599,000	606,114	215,447	199,588	191,079
Production 2025 (ytd) (kWh)	6,524,000	6,364,788	2,215,909	2,151,618	1,997,261
Total Production (LTM) (kWh)	11,708,000	10,493,604	3,651,290	3,503,801	3,338,513
Capacity Factor (LTM)	26.62%				

B. Site Energy Production Graph

June-2025

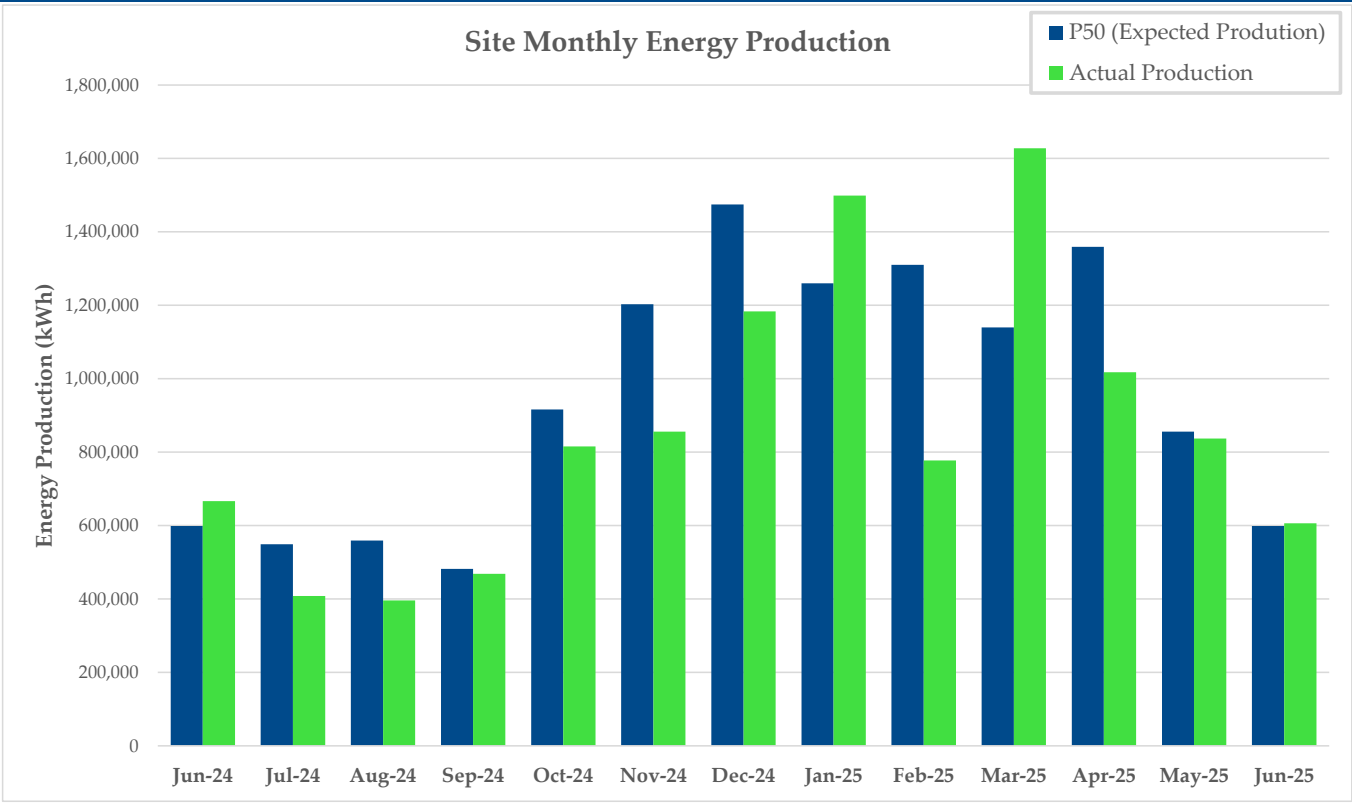

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
July-2025	9 Year Turbine Preventive Maintenance	~8	Z1
July-2025	9 Year Turbine Preventive Maintenance	~8	Z2
July-2025	9 Year Turbine Preventive Maintenance	~8	Z3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
6/10/2025	Customer Shutdown	Unplanned	7.08	Z1
6/11/2025	Customer Shutdown	Unplanned	8.55	Z3
6/13/2025	Customer Shutdown	Unplanned	6.49	Z1
6/25/2025	Customer Shutdown	Unplanned	6.00	Z3

F. Turbine Downtime and Uptime¹

Downtime (hr)	This Month	Year To Date
Z1	17.80	196.24
Z2	2.84	107.93
Z3	17.38	208.48
Total	38.02	512.65

Uptime (hrs)	Life Time
Z1, Z2, Z3	82512.00

G. Billed Data

Meter Reading (Date/Time)	6/19/2025 12:00 AM
Ball 1.0 Production (This Period)	657,505 kWh
Ball 1.0 Consumption (This Period)	891 kWh
Billed kWh	656,614 kWh
Next Meter Reading	7/19/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Downtime and Uptime Pending.

² Z1 derated to 1000 kW for 4.32 hours on Dec 17
