


A. Site Energy Production Summary

		Energy Production (kWh)					
		Site		By Turbine			
		P50 (Expected Production)	Actual Production	WG1	WG2		WG3
	Jun-24	714,000	457,519	234,750	0	222,769	2
	Jul-24	566,000	306,010	138,508	26,329	141,173	
	Aug-24	514,000	412,680	141,710	134,341	136,629	3
	Sep-24	716,000	531,587	183,534	168,417	179,636	
	Oct-24	1,051,000	881,013	307,605	290,645	282,763	
	Nov-24	1,224,000	1,122,327	391,525	369,519	361,283	
	Dec-24	1,217,000	1,260,023	446,812	416,052	397,159	
	Jan-25	1,343,000	1,398,943	512,624	450,432	435,887	
	Feb-25	1,133,000	710,891	253,926	229,140	227,825	
	Mar-25	1,312,000	1,642,126	558,314	545,778	538,034	
	Apr-25	1,272,000	1,161,033	398,359	383,282	379,392	
	May-25	974,000	820,580	290,223	244,974	285,383	
	Jun-25	714,000	475,454	164,257	156,803	154,394	
Production 2025 (ytd) (kWh)		6,748,000	6,209,027	2,177,703	2,010,409	2,020,915	
Total Production (LTM) (kWh)		12,036,000	10,722,667	3,787,397	3,415,712	3,519,558	
Capacity Factor (LTM)		27.20%					

B. Site Energy Production Graph

June-2025

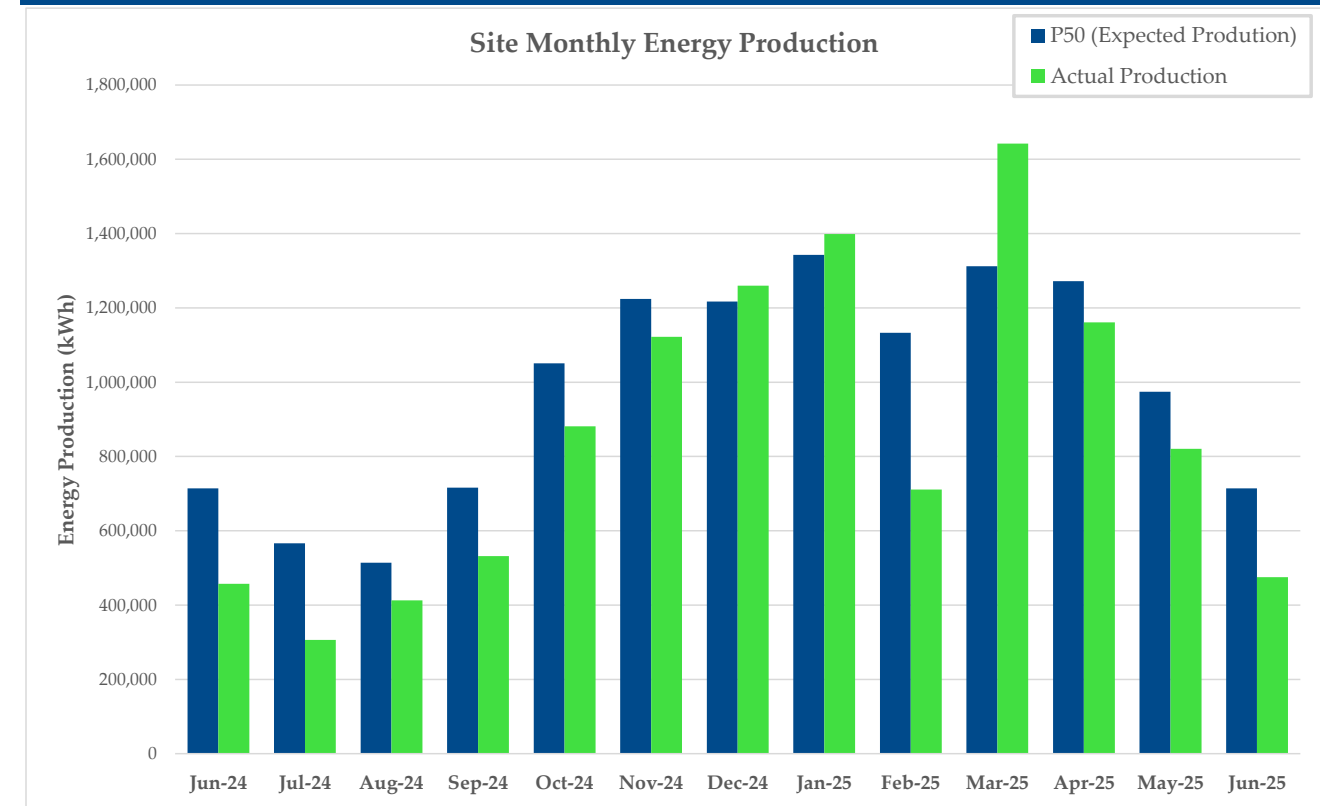

Monthly Report
June-2025

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
First Aid	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
July-2025	6.5 Year Preventive Maintenance	~15	WG 1
July-2025	6.5 Year Preventive Maintenance	~15	WG 2
July-2025	6.5 Year Preventive Maintenance	~15	WG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
6/21/2025-6/22/2025	Plant Shutdown	Unplanned	25.69	WG1, WG2, WG3

F. Turbine Downtime and Uptime¹

Downtime (hr)	This Month	Year To Date
WG1	28.84	243.70
WG2	29.03	279.24
WG3	28.82	229.34
`	86.69	752.28

Uptime (hrs)	Life Time
WG1, WG2, WG3	58512.00

G. Billed Data

Meter Reading (Date/Time)	6/29/2025 12:00 AM
Meter To Date Produced	68,287,403 kWh
Meter To Date Consumed	284,543 kWh
Last Reading Produced	67,753,140 kWh
Last Reading Consumed	280,070 kWh
Billed kWh	529,790 kWh
Next Meter Reading	7/29/2025 12:00 AM

H. Report Notes and Comments

¹ Turbine Downtime and Uptime Pending.
² As a result of previously disclosed circumstances, WG 2 had no energy production February 2024 - June 2024.
³ W2 was derated to 250 KW for .62hrs on Feb 13 for testing
