


A. Site Energy Production Summary

	Energy Production (kWh)					*
	Site		By Turbine			
	Expected Production	Actual Production	WTG 1	WTG 2	WTG 3	
Sep-22	603,085	395,973	133,364	128,586	134,023	
Oct-22	967,926	1,373,420	466,421	429,871	477,128	
Nov-22	1,362,692	1,568,093	527,267	521,360	519,466	
Dec-22	1,254,397	1,487,190	491,635	498,005	497,550	
Jan-23	1,290,968	1,253,314	423,857	413,023	416,434	
Feb-23	1,170,349	1,453,948	522,598	439,412	491,938	
Mar-23	1,227,217	1,298,079	501,593	304,805	491,681	
Apr-23	1,438,497	1,155,788	408,089	343,589	404,110	
May-23	980,450	753,863	252,701	233,602	267,560	
Jun-23	649,158	683,362	231,589	228,457	223,316	
Jul-23	618,687	440,827	132,214	148,791	159,822	
Aug-23	559,508	555,831	128,322	211,051	216,458	
Sep-23	603,085	353,794	138,579	132,576	82,639	
Production 2023 (ytd) (kWh)	8,537,920	7,948,806	2,739,542	2,455,306	2,753,958	
Total Production (LTM) (kWh)	12,122,935	12,377,509	4,224,865	3,904,542	4,248,102	
Capacity Factor (LTM)	31.40%					

B. Site Energy Production GraphSeptember-2023

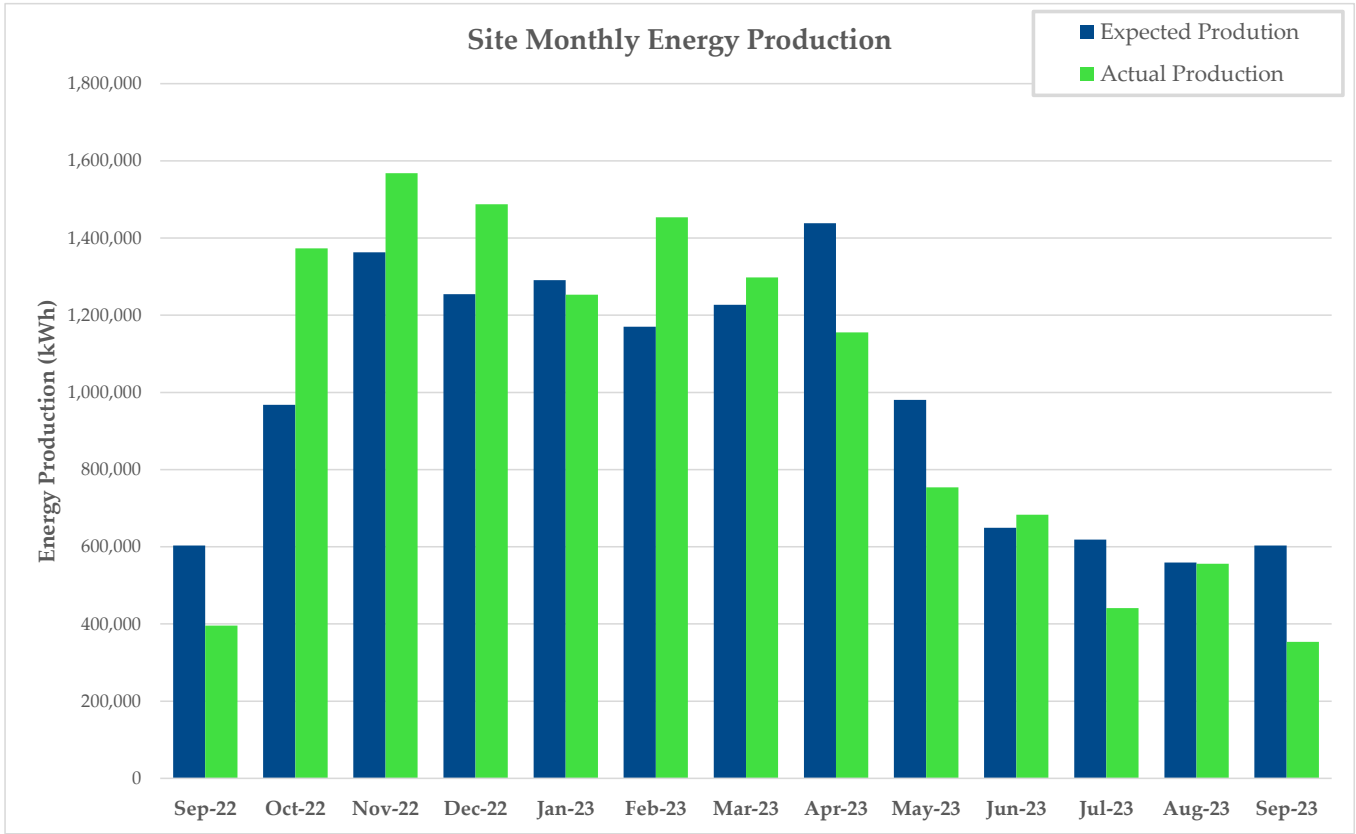

Monthly ReportSeptember-2023

C. Safety Summary

	This Month	Project Cumulative
Recordable Incident(s)	0	0
Near Miss(es)	0	0

D. Planned Maintenance Events

Date	Event	Duration (hr)	Turbine
November-2023	11 Year Maintenance	~15	WTG 1
November-2023	11 Year Maintenance	~15	WTG 2
November-2023	11 Year Maintenance	~15	WTG 3

E. Actual Maintenance Events

Date	Event	Planned/Unplanned	Duration (hrs)	Turbine
9/1/2023	Blade Repair	Unplanned	25.32	WTG 1
9/2/2023-9/3/2023	Blade Repair	Unplanned	16.9	WTG 2
9/2/2023	Blade Repair	Unplanned	8.73	WTG 3
9/4/2023	Blade Repair	Unplanned	16.32	WTG 3
9/5/2023-9/7/2023	Blade Repair	Unplanned	55.29	WTG 2
9/7/2023	Blade Repair	Unplanned	6.20	WTG 3
9/9/2023-9/10/2023	Blade Repair	Unplanned	33.91	WTG 3
9/11/2023-9/13/2023	Blade Repair	Unplanned	56.43	WTG 3
9/11/2023-9/13/2023	Blade Repair	Unplanned	56.13	WTG 1
9/14/2023-9/16/2023	Blade Repair	Unplanned	47.09	WTG 1
9/14/2023	Blade Repair	Unplanned	10.83	WTG 3
9/15/2023-9/16/2023	Blade Repair	Unplanned	18.74	WTG 3
9/16/2023	Blade Repair	Unplanned	10.08	WTG 2
9/18/2023	Blade Repair	Unplanned	11.24	WTG 3
9/18/2023-9/19/2023	Blade Repair	Unplanned	31.95	WTG 2
9/19/2023-9/20/2023	Blade Repair	Unplanned	23.59	WTG 3
9/20/2023-9/21/2023	Blade Repair	Unplanned	32.52	WTG 2
9/22/2023-9/25/2023	Blade Repair	Unplanned	54.04	WTG 2
9/29/2023-9/30/2023	Blade Repair	Unplanned	40.75	WTG 2

F. Turbine Availability & Downtime**

Availability	This Month	Year To Date
WTG 1	100.00%	100.00%
WTG 2	100.00%	100.00%
WTG 3	100.00%	99.99%
Avg	100.00%	100.00%

Downtime (hr)	This Month	Year To Date
WTG 1	133.67	688.36
WTG 2	248.57	828.12
WTG 3	182.48	272.15
Total	564.82	1788.63

G. Wind Speed & Capacity Factor

Wind Speed (mph)	This Month	2022 Annual
WTG 1	4.94	14.41
WTG 2	4.90	14.29
WTG 3	4.97	14.49
Estimated	11.09	13.39

Capacity Factor (%)	This Month	2022 Annual
WTG 1	12.83%	44.69%
WTG 2	12.28%	35.72%
WTG 3	7.65%	43.21%
Low Estimate	18.42%	28.72%

H. Report Notes and Comments

* September 2022 production is lower than actual due to SCADA communication issues.
**Due to expiration of the OEM warranty, turbine availability and downtime reporting will no longer include warranted availability. Downtime will be categorized appropriately. One Energy will update future reports to reflect this change.
